



Artifex Construction Corporation
 4913 SW 75th Ave
 Miami, Florida 33155
 P: (305)521-9090
 F: (305)521-9085

Project: 21-253 - 2700 Ponce De Leon Improvements
 2700 Ponce De Leon Boulevard
 Coral Gables, Florida 33134

Daily Log: Monday 4/24/2023



Daily Log Completed

The Daily Log was completed by Carlos Lopez on Mon, May 1, 2023 at 11:30 AM EDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
72°F	80°F	75°F	0.07 in.	0.07 in.	0.07 in.	72%	82%	94%	70°F	3.1 mph	5 mph	13 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
Partly Cloudy 72°F	Cloudy 79°F	Cloudy 77°F	Cloudy 78°F	Cloudy 78°F	Clear 76°F

OBSERVED WEATHER CONDITIONS

No.	Time Observed	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea
1	10:15:00 AM	No						

MANPOWER LOG

15 Workers | 120.0 Man Hours

No.	Contact/Company	Workers	# Hours	Man Hours	Location
1	Artifex Construction Corp.	8	8.0	64.0	
Notes: Demolition of the existing column on the second floor was started , this is additional scope not previously contracted. Began stripping of the form work from the areas which concrete was poured on Friday Continued with installing form work for the areas which concrete will be poured next.					
2	Artifex Construction Corp.	1	8.0	8.0	
Notes: Supervisor					
3	BOLD CONSTRUCTION SPECIALTIES INC	6	8.0	48.0	
Notes: Stucco contractor worked on the exterior of the elevator equipment room , and the surrounding parapet					
		15	120.0		

Manpower Log's Attachments:


1. Artifex Construction Corp.



[IMG_7410.jpeg](#)



[IMG_7409.jpeg](#)

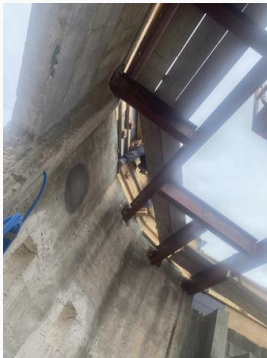

[IMG_7406.jpeg](#)



[IMG_7405.jpeg](#)

3. BOLD CONSTRUCTION SPECIALTIES INC

[IMG_7412.heic](#) [IMG_7411.heic](#)

By

Date

Copies To
